SAMPLE
Project Plan

Computer Science Project

Spring 2019

Table of Contents

Introduction 3
Statement of Work 3
Resource List 4
Roles 4
Risks 5
Schedule 6

1. Introduction

The Project Plan document for the group project that will be used to provide a statement of how and when the project's objectives will be achieved. Included in the document are: Statement of Work, Resource List, Roles, Risks, and Schedule.

2. Statement of Work

The client, Computer Science Department, has requested us to develop a website with two main purposes. First, students will be allowed to check their grades of all of the computer science courses they are enrolled in. Second, students will also be allowed to submit their course assignments electronically via website. Teaching Assistants will be responsible for creating/inserting the grades for each individual student in the course as well as creating the submission for each assignment for each course that they are assigned to.

3. Resource List

In order to create the website, several resources must be acquired by the team to accomplish the task:

1) Computer Science Department Server (Some Linux Server)
2) Personal/CS Lab computers for programming (Possible Linux/Windows XP Operating System)
3) Web-based programming tool (May be using PHP)
4) Database software (Possible to use MySQL Sever 2008)
5) Internet Access (LAN/Wi-Fi is needed) 6) Paper/Online resources (TBD)

4. Roles

With such a limited amount of personal to accomplish the project, each team member will be responsible for multiple roles in order to complete the project on time.

Role	Team Leader
Member	Mr. Jones
Description	This person is responsible for managing the team. He is responsible for contacting the client about any updates/issues that occur throughout the project. Ensures all deadlines are completed.

Role	Programmer
Member	Mr. Jones, Donald Duke
Description	The programmer is responsible for writing the code for the project.

Role	User Interface Designer
Member	Donald Duke, Mikey Mud
Description	These individuals will be responsible for designing a graphical user interface for the project. This is a key role since the individuals are developing a web page and as such, the interface must be clean.

Sample CMSC 495 Project Plan

5. Risks

This section contains many of the risks involved with creating such a big project with limited personal. Being able to identify these risks right now will allow us to prepare ourselves ahead of time so that when we begin programming, these risks will not be as critical as they once were.

Risk	Probability	Impact	Action
Unfamiliarity with specific programming languages.	90%	Not knowing the programming languages we will be using will cause a major breakdown in our schedule and would result in a stoppage of all work.	Familiarize ourselves with the languages that we will be using so we will be prepared.
Unfamiliarity with Linux Administration	80%	Since the server is ran on a Linux Server, not understanding how a Linux Server operates would cause major problems.	Familiarize ourselves with several Linux Administration operations via website/books so we can be prepared for any problems that might occur
Team Availability	50%	Being unable to meet as a team would cause us to be behind in our schedule because of our conflicting schedules.	Try to find anytime, even if it is very brief, to discuss what we have accomplished and what we will need to accomplish in the future.

6. Schedule

Sample CMSC 495 Project Plan

The Gantt Chart below is a tentative schedule of our plans for the remainder of the current semester and next semester. We will be using this schedule to make sure we stay on focus, however; plans are not set completely and therefore might be changed before spring semester begins.

Computer Science Gradebook Gannt Chart			
Tasks	**Start Date**	**Duration(Days)**	**End Date**
1 Planning/Design	11/10/2019	35	12/15/2019
1.1 Project Definition	11/10/2019	7	11/17/2019
1.2 Finish Webpage	11/17/2019	23	12/10/2019
1.3 Project Design	11/17/2019	28	12/15/2019
2 Coding	1/11/2019	88	4/9/2019
2.1 Phase 1	1/11/2019	42	2/22/2019
2.2 Phase 2	3/7/2019	12	3/19/2019
2.3 Additional Features	3/26/2019	14	4/9/2019
3 Testing	2/22/2019	58	4/21/2019
3.1 Phase 1 Testing	2/22/2019	11	3/5/2019
3.2 Phase 2 Testing	3/19/2019	7	3/26/2019
3.3 Final Testing	4/9/2019	12	4/21/2019
4 Documentation	4/21/2019	16	5/7/2019
4.1 User Guide	4/21/2019	12	5/3/2019
4.2 Presentation	5/3/2019	4	5/7/2019
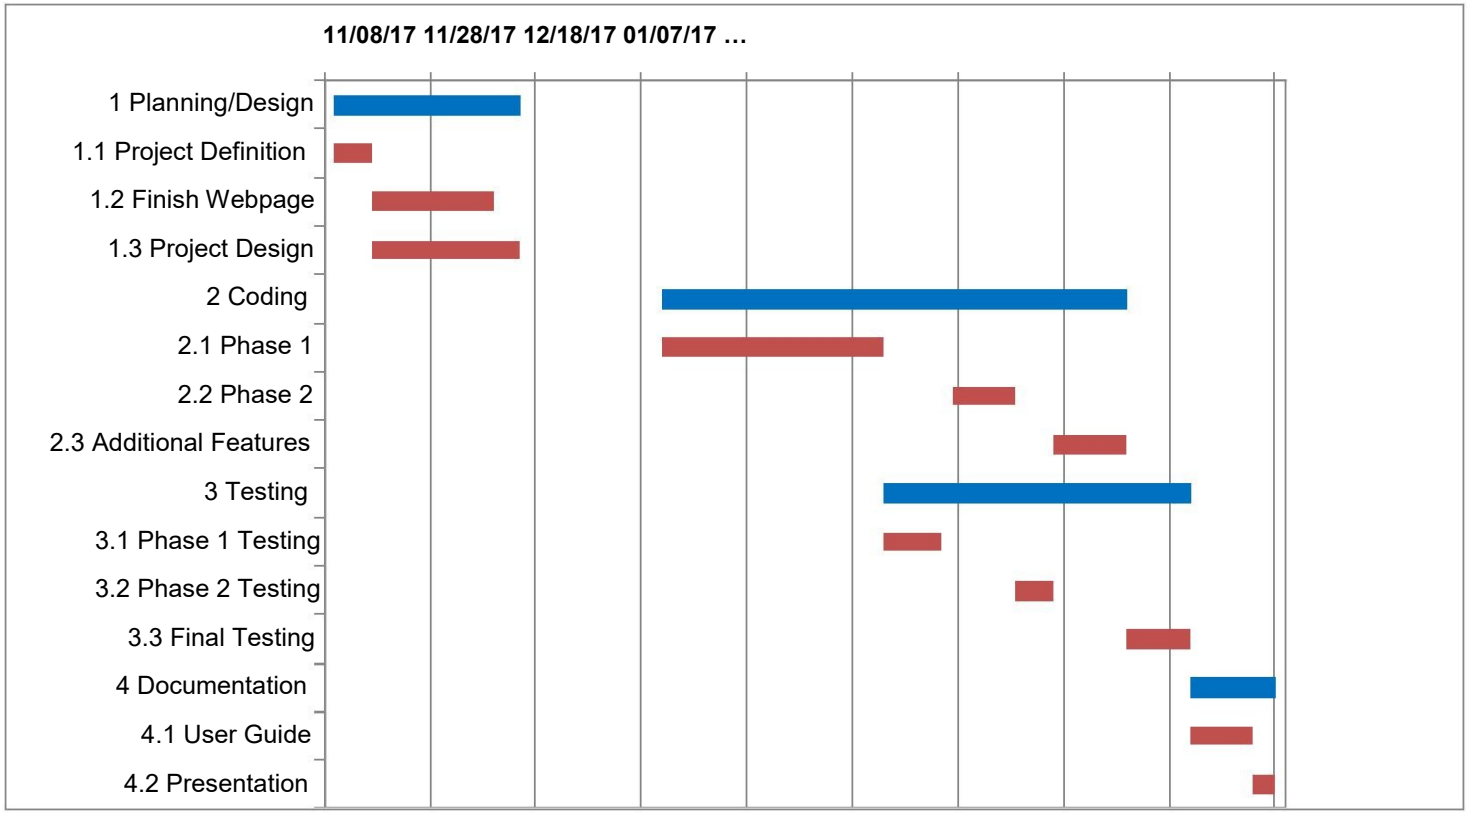
Sample CMSC 495 Project Plan
